


# AACE-PSP Certification Training & AACE-PSP Study Guide & AACE-PSP Best Questions

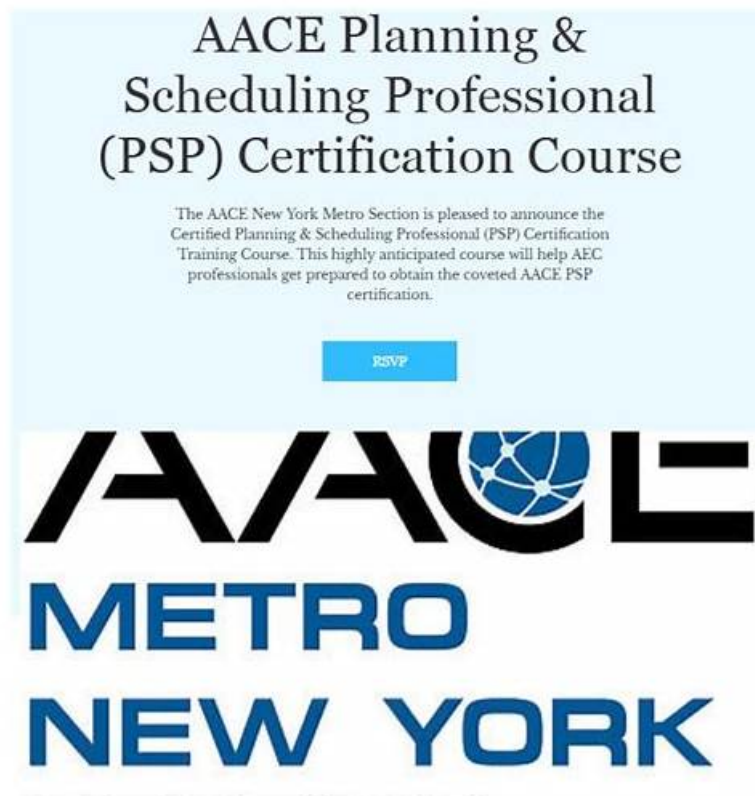

2025 Latest DumpExam AACE-PSP PDF Dumps and AACE-PSP Exam Engine Free Share: [https://drive.google.com/open?id=1QhDTR5A0PyKZdEj0xH\\_HgOxOOO\\_yOTeC](https://drive.google.com/open?id=1QhDTR5A0PyKZdEj0xH_HgOxOOO_yOTeC)

One of the reason for this popularity is our study material are accompanied by high quality and efficient services so that they can solve all your problems. We guarantee that after purchasing our AACE-PSP test prep, we will deliver the product to you as soon as possible about 5-10 minutes. So you don't need to wait for a long time or worry about the delivery time has any delay. We will transfer our AACE-PSP Test Prep to you online immediately, and this service is also the reason why our AACE-PSP study torrent can win people's heart and mind.

DumpExam provides Planning & Scheduling Professional (PSP) Exam AACE-PSP desktop-based practice software for you to test your knowledge and abilities. The Planning & Scheduling Professional (PSP) Exam AACE-PSP desktop-based practice software has an easy-to-use interface. You will become accustomed to and familiar with the free demo for Planning & Scheduling Professional (PSP) Exam AACE-PSP Exam Questions. Exam self-evaluation techniques in our Planning & Scheduling Professional (PSP) Exam AACE-PSP desktop-based software include randomized questions and timed tests. These tools assist you in assessing your ability and identifying areas for improvement to pass the Planning & Scheduling Professional (PSP) Exam certification exam.

>> AACE-PSP New Soft Simulations <<

## Quiz 2025 AACE International AACE-PSP: Planning & Scheduling Professional (PSP) Exam New Soft Simulations

DumpExam can provide a shortcut for you and save you a lot of time and effort. DumpExam will provide good training tools for your AACE International Certification AACE-PSP Exam and help you pass AACE International certification AACE-PSP exam. If you see other websites provide relevant information to the website, you can continue to look down and you will find that in fact the information is mainly derived from our DumpExam. Our DumpExam provide the most comprehensive information and update fastest.

The AACE-PSP certification exam covers a wide range of topics related to project planning and scheduling, including project

planning, scheduling, resource allocation, cost control, and risk management. AACE-PSP exam is designed to test the candidate's understanding and application of these concepts in real-world scenarios. AACE-PSP exam consists of multiple-choice questions and is administered in a secure, proctored environment.

The AACE-PSP Certification is designed for individuals who specialize in planning, scheduling, and project management. Planning & Scheduling Professional (PSP) Exam certification program is ideal for professionals seeking to enhance their skills in project planning and scheduling, Cost management, Risk Management, Effective communication, and other related fields. The AACE-PSP Certification program aims to educate individuals about fundamental project management concepts and practices that will help them excel in their professional careers.

## AACE International Planning & Scheduling Professional (PSP) Exam Sample Questions (Q45-Q50):

### NEW QUESTION # 45

A good change management plan \_\_\_\_\_.

- A. is provided to stakeholders after it is created
- B. involves only the project controls team
- C. tracks minor decisions
- D. is detailed during the planning phase

**Answer: D**

Explanation:

Best Practices for Change Management Plans:

Effective plans are developed in the planning phase, ensuring all stakeholders understand how changes will be managed.

Evaluation of Options:

Option A: Incorrect. Stakeholders are involved during development, not just after.

Option C: Incorrect. A change management plan focuses on significant changes, not minor decisions.

Option D: Incorrect. It involves all stakeholders, not just the project controls team.

Option B: Correct. Change management plans are part of project planning.

Reference:

PSP Study Guide (2019), Sections on Critical Path Analysis, Float Management, and Change Management.

AACE Recommended Practices, RP 10S-90.

### NEW QUESTION # 46

These are the activities on the critical path:



- A, A, C, E, & H.
- **B, A, B, G, & H.**
- C, A, B, F, & J
- D, A, D, & I.

**Answer: B**

Explanation:

\* Critical Path Identification:

The critical path is the longest sequence of activities that determines the project's minimum duration.

Path: A → B → G → H.

\* Exclusion of Other Options:

Paths involving F, J, or non-critical activities do not align with the longest duration.

\* Verification with PSP Guidelines:

The PSP Study Guide emphasizes identifying the critical path for schedule optimization (Ref: PSP Study Guide, Chapter 2A: Critical Path Analysis)

#### NEW QUESTION # 47

In a "crashed" schedule, which is a chain of activities that precede activity 2004?

| ID   | Activity                    | Logic                                |                            |                      | Normal Schedule |              | Crashed Schedule |              |
|------|-----------------------------|--------------------------------------|----------------------------|----------------------|-----------------|--------------|------------------|--------------|
|      |                             | Succ.                                | Rel.                       | Lag                  | Days            | Direct Costs | Days             | Direct Costs |
| 1000 | General Conditions          | 11001                                | FF                         |                      | 1072            | \$3,080,000  | 910              | \$2,902,900  |
| 1001 | Preliminary Civil Work      | 1000<br>2001<br>7001                 | SS<br>FS<br>FS             |                      | 85              | \$563,000    | 67               | \$728,000    |
| 2001 | River Diversion Stage 1     | 2002                                 | FS                         |                      | 92              | \$150,000    | 75               | \$190,000    |
| 2002 | River Diversion Stage 2     | 2003                                 | FS                         |                      | 38              | \$25,000     | 28               | 35,000       |
| 2003 | River Diversion Dam         | 2004<br>3001                         | FS<br>FS                   |                      | 15              | \$18,000     | 11               | \$20,000     |
| 2004 | River Diversion to Pipeline | 3001<br>7001                         | FS<br>FS                   |                      | 38              | \$96,000     | 38               | \$96,000     |
| 3001 | Excavation, Dam Site        | 4001<br>4001<br>5001<br>5001<br>7001 | SS<br>FF<br>SS<br>FF<br>FS | 15<br>15<br>65<br>65 | 30              | \$482,000    | 100              | \$515,000    |
| 4001 | Excavation, Spillway        | 5001<br>5001<br>9001                 | SS<br>FF<br>FS             | 45<br>45             | 152             | \$608,000    | 118              | \$692,000    |
| 5001 | Drill and Grout Dam Site    | 6001                                 | FS                         |                      | 102             | \$637,000    | 92               | \$650,000    |
| 6001 | Rock Fill: to elevation 25  | 6002                                 | FS                         |                      | 140             | \$1,352,000  | 105              | \$1,470,000  |
| 6002 | Rock Fill: to elevation 38  | 6003                                 | FS                         |                      | 115             | \$969,000    | 95               | \$1,125,000  |
| 6003 | Rock Fill: to elevation 50  | 8001<br>9002<br>9002<br>9003         | FS<br>SS<br>FF<br>FS       | 65<br>65             | 152             | \$1,360,000  | 113              | \$1,540,000  |

|       |                                |                       |                |   |     |             |     |             |
|-------|--------------------------------|-----------------------|----------------|---|-----|-------------|-----|-------------|
| 7001  | Permanent Roads                | 11001<br>9004         | FS<br>FS       |   | 48  | \$180,000   | 38  | \$205,000   |
| 8001  | Valve House Embankment         | 9004                  | FS             |   | 28  | \$28,000    | 22  | \$36,000    |
| 9001  | Spillway – Concrete            | 11001<br>9002<br>9003 | FS<br>FS<br>FS |   | 175 | \$1,120,000 | 155 | \$1,305,000 |
| 9002  | Dam Concrete Facing – Concrete | 1001<br>9005          | FS<br>FS       |   | 180 | \$1,260,000 | 160 | \$1,485,000 |
| 9003  | Inlet Tower – Concrete 1 of 2  | 9005                  | FS             | 7 | 70  | \$275,000   | 65  | \$295,000   |
| 9004  | Valve House – Concrete         | 10002                 | FS             | 7 | 72  | \$245,000   | 66  | \$265,000   |
| 9005  | Inlet Tower – Concrete 2 of 2  | 10001                 | FS             | 7 | 35  | \$28,000    | 35  | \$28,000    |
| 10001 | Inlet Tower – Complete         | 11001                 | FS             |   | 25  | \$147,000   | 25  | \$147,000   |
| 10002 | Valve House –                  | 10001                 | FS             |   | 24  | \$132,000   | 24  | \$133,000   |

- A. 1001, 2002, 2002, 2003, 3001
- B. 2001, 2002, 2003, 2007
- C. 1001, 2001, 2002, 2003
- D. 1001, 2002, 2003

**Answer: C**

Explanation:

\* Crashed Schedule Predecessors to Activity 2004:

Activity 2004 (River Diversion to Pipeline) depends on completion of:

1001 (Preliminary Civil Work).

2001 (River Diversion Stage 1).

2002 (River Diversion Stage 2).

2003 (River Diversion Dam).

\* Exclusion of Other Activities:

Activity 2007 is not part of the crashed schedule's direct predecessor chain.

Other options include duplicated or incorrect entries.

\* PSP Study Guide Reference:

Logical sequence analysis confirms these predecessors (Ref: PSP Study Guide, Chapter 2A: Activity Sequencing and Critical Path Analysis).

#### NEW QUESTION # 48

If after calculating a schedule an activity exhibits negative total float, which of the following is certain? The activity

- A. Is a milestone.
- B. It is on the critical path.
- C. Has yet to be completed.
- D. Was completed in the past.

**Answer: C**

Explanation:

Negative total float occurs when an activity's scheduled completion date extends beyond the project deadline due to constraints.

This condition indicates that the activity is still pending and needs immediate attention to avoid further delays.

Option A (milestone) is unrelated.

Option B (critical path) is not necessarily true, as activities with negative float can exist off the critical path under certain constraints.

Option C (completed in the past) is incorrect as negative float applies only to future or ongoing activities.

### NEW QUESTION # 49

Which of the following will NOT affect the total float calculation of a non-resource leveled schedule?

- A. Multiple calendars.
- B. Preferential logic.
- C. Front end loading.
- D. Start and finish constraints.

**Answer: C**

### NEW QUESTION # 50

• • • • •

AACE-PSP Guide Quiz helped over 98 percent of exam candidates get the certificate. Before you really attend the AACE International AACE-PSP exam and choose your materials, we want to remind you of the importance of holding a certificate like this one. Obtaining a AACE International AACE-PSP certificate likes this one can help you master a lot of agreeable outcomes in the future, like higher salary, the opportunities to promotion and being trusted by the superiors and colleagues.

**Download AACE-PSP Free Dumps:** <https://www.dumpexam.com/AACE-PSP-valid-torrent.html>

- Smashing AACE-PSP Guide Materials: Planning & Scheduling Professional (PSP) Exam supply you high-efficient Exam Brain Dumps - www.examcollectionpass.com □ Search for { AACE-PSP } and easily obtain a free download on 「www.examcollectionpass.com」 □AACE-PSP Test Price
- Latest AACE-PSP Exam Papers □ Demo AACE-PSP Test □ AACE-PSP Popular Exams □ Search for ► AACE-PSP □ and download it for free immediately on ➡ www.pdfvce.com □ □Test AACE-PSP Questions
- Valid AACE-PSP Exam Sims □ AACE-PSP Latest Exam Format □ AACE-PSP Training Tools □ Search for ► AACE-PSP ◀ and download it for free on □ www.testkingpdf.com □ website □AACE-PSP Reliable Exam Papers
- AACE-PSP Popular Exams □ Valid Brindumps AACE-PSP Book □ AACE-PSP Latest Test Prep □ Simply search for▷ AACE-PSP ◁ for free download on ➡ www.pdfvce.com □□□ □Exam AACE-PSP Format
- Exam AACE-PSP Online □ AACE-PSP Latest Test Prep □ Valid AACE-PSP Exam Sims □ Easily obtain free download of⇒ AACE-PSP ⇐ by searching on ✓ www.pass4test.com □✓□ □AACE-PSP Reliable Exam Papers
- Top AACE-PSP New Soft Simulations | Valid AACE-PSP: Planning & Scheduling Professional (PSP) Exam 100% Pass □ □ Go to website 【 www.pdfvce.com 】 open and search for ☼ AACE-PSP □☼□ to download for free □AACE-PSP Reliable Exam Papers
- Realistic AACE-PSP New Soft Simulations - Find Shortcut to Pass AACE-PSP Exam □ Search for ✓ AACE-PSP □✓□ and obtain a free download on ☼ www.pass4leader.com □☼□ □AACE-PSP Latest Test Prep
- Use Real AACE-PSP Dumps Guaranteed Success □ Immediately open ☼ www.pdfvce.com □☼□ and search for “ AACE-PSP ” to obtain a free download □Valid AACE-PSP Test Preparation
- Valid AACE-PSP Test Preparation □ Valid AACE-PSP Exam Sims □ Exam AACE-PSP Format □ Easily obtain ➡ AACE-PSP □□□ for free download through （ www.testsimulate.com ） □AACE-PSP Reliable Exam Papers
- Valid Brindumps AACE-PSP Book □ AACE-PSP Training Tools □ AACE-PSP Training Tools □ Open 「 www.pdfvce.com 」 and search for { AACE-PSP } to download exam materials for free □AACE-PSP 100% Correct Answers
- Realistic AACE-PSP New Soft Simulations - Find Shortcut to Pass AACE-PSP Exam □ Easily obtain ✓ AACE-PSP □✓□ for free download through ⇒ www.prep4pass.com ⇐ □AACE-PSP Test Price
- www.stes.tyc.edu.tw, www.lcdpt.com, www.stes.tyc.edu.tw, myportal.utt.edu.tt, myportal.utt.edu.tt, myportal.utt.edu.tt, myportal.utt.edu.tt, myportal.utt.edu.tt, myportal.utt.edu.tt, myportal.utt.edu.tt, myportal.utt.edu.tt, 121.40.19.218:89, lms.abe.institute, www.stes.tyc.edu.tw, www.stes.tyc.edu.tw, myportal.utt.edu.tt, myportal.utt.edu.tt, myportal.utt.edu.tt, myportal.utt.edu.tt, myportal.utt.edu.tt, myportal.utt.edu.tt, Disposable vapes

BTW, DOWNLOAD part of DumpExam AACE-PSP dumps from Cloud Storage: [https://drive.google.com/open?id=1QhDTR5A0PykZdEj0xH\\_HgOxOOO\\_vOTeE](https://drive.google.com/open?id=1QhDTR5A0PykZdEj0xH_HgOxOOO_vOTeE)
