

Prominent Features of AACE International AACE-PSP Practice Exam Material



AACE International

*AACE-PSP
Planning & Scheduling Professional (PSP) Exam*

Questions & Answers PDF

For More Information:
<https://www.certswarrior.com/>

Features:

- 90 Days Free Updates
- 30 Days Money Back Guarantee
- Instant Download Once Purchased
- 24/7 Online Chat Support
- Its Latest Version

Visit us at <https://www.certswarrior.com/exam/aace-psp/>

P.S. Free & New AACE-PSP dumps are available on Google Drive shared by ActualVCE: https://drive.google.com/open?id=1VK1gWUEYsS9svRa7Q5x_fhHEBo1wn-6r

Our product is revised and updated according to the change of the syllabus and the latest development situation in the theory and the practice. The AACE-PSP exam torrent is compiled elaborately by the experienced professionals and of high quality. The contents of AACE-PSP guide questions are easy to master and simplify the important information. It conveys more important information with less answers and questions, thus the learning is easy and efficient. The language is easy to be understood makes any learners have no obstacles. The AACE-PSP Test Torrent is suitable for anybody no matter he or she is in-service staff or the student, the novice or the experience people who have worked for years. The software boosts varied self-learning and self-assessment functions to check the results of the learning.

AACE International AACE-PSP Certification program covers various aspects of planning and scheduling, including project economics, budgeting, forecasting, progress monitoring, and risk management. The program has been developed keeping in mind the evolving needs of the industry, and it combines the latest best practices with practical knowledge and experience.

>> Test AACE-PSP Engine <<

Reliable Test AACE-PSP Engine, Ensure to pass the AACE-PSP Exam

ActualVCE offers 100% secure online purchase at all the time. We offer payments through Paypal-one of the most trusted payment providers which can ensure the safety shopping for AACE-PSP study torrent. Besides, before you choose our material, you can try our AACE-PSP free demo questions to check if it is valuable for you to buy our AACE-PSP practice dumps. You will get the latest and updated study dumps within one year after your purchase. So, do not worry the update and change in the actual test, you will be confident in the real test with the help of our AACE-PSP training torrent.

To be eligible to take the PSP certification exam, candidates must meet certain educational and experience requirements. Candidates must have a minimum of four years of professional experience in project planning and scheduling, as well as a bachelor's degree or equivalent in a related field. Candidates who do not have a degree may still be eligible to take the exam if they have at least eight years of professional experience in project planning and scheduling.

AACE International Planning & Scheduling Professional (PSP) Exam Sample Questions (Q187-Q192):

NEW QUESTION # 187

Before the work begins, the contractor considers crashing the schedule. How much would the crashed general conditions have to be reduced to break even with the normal cost budget?

Normal Total Cost	12,990,000
Crashed Total Cost	13,102,900
Normal Overhead Cost	3,080,000
Crashed Overhead Cost	2,902,900



- A. \$195 per day
- B. General conditions do not need to be reduced to break even
- C. \$1.223 per day
- **D. \$1.772 per day**

Answer: D


NEW QUESTION # 188

Identify the late finish to develop plans and specs.

Refer to the following table and diagram to answer the following questions. Consider this to be the entire network. The diagram is incomplete. This table represents activities, predecessors and durations for a hazardous waste incineration facility.

INTERNATIONAL

Activity	Description	Predecessors	Duration (months)
A	Develop information for public hearings	-	3
B	Hold public hearings	A	3
C	Develop draft plans and specifications	A	5
D	Contact stakeholders and others	A	7
E	Obtain permits	B, C	3
F	Order equipment for facility	B	4
G	Procure and prepare land.	B	6
H	Construct facility	D, E, F & G	8
I	Approval of operating procedures	D	6
J	Install equipment, staff, faculty	F	9

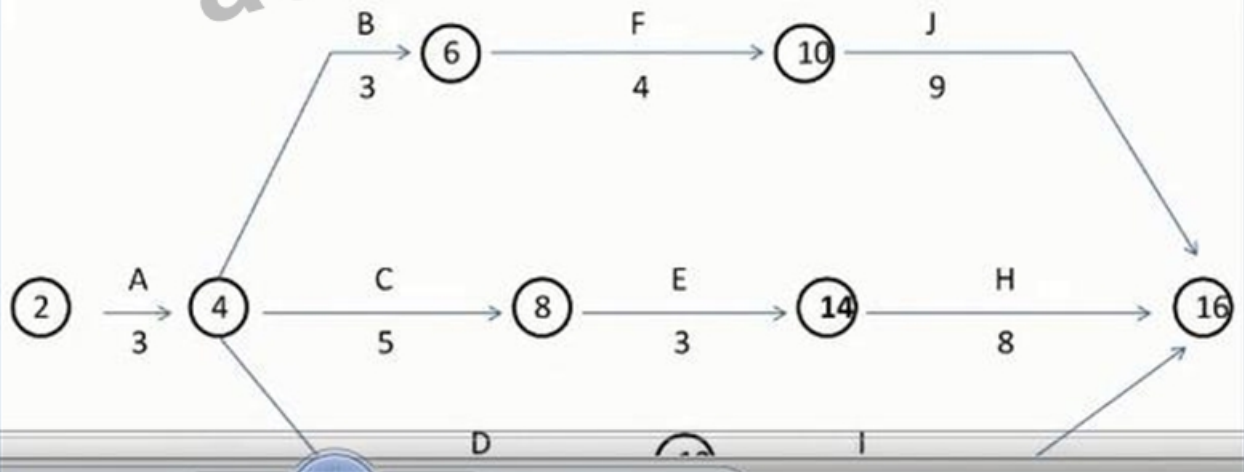

- A. 8 months.
- **B. 10 months.**
- C. 9 months.
- D. 7 months.

Answer: B

Explanation:

* Late Finish Analysis for Activity C (Develop Plans and Specs):

Activity C duration is 5 months, starting after Activity A (3 months).

Late finish = Early start of successor (Activity E) = 10 months.

* Cross-Verification:

Based on backward pass calculations, Activity C must end by month 10 to not delay its successor.

* Verification with PSP Guidelines:

Late finish values are calculated during backward pass (Ref: PSP Study Guide, Chapter 2A: Backward Pass and Float Calculations).

NEW QUESTION # 189

Due to a testing delay, release of the product for manufacture is delayed by 5 workdays and the product manual misses its print window at the printer. If the printer is delayed by 10 workdays, what is the delay to produce release?

- A. 0 days.
- B. 5 days.
- C. 10 days.
- D. 15 days.

Answer: D

Explanation:

* Situation Analysis:

A 5-day delay in product release impacts the printing window.

The printer is further delayed by 10 workdays.

* Total Delay Impact Calculation:

The combined impact of the testing and printing delays = $5 + 10 = 15$ days.

This results in a cumulative delay in product release.

* Cross-Verification:

Option B: Incorrect. Ignores delays entirely.

Option C: Incorrect. Assumes only one source of delay.

Option D: Incorrect. Underestimates delay impact.

Option A: Correct. Matches the calculated total delay.

NEW QUESTION # 190

Using the normal schedule, given Activity 3001 and the relationship with Activity 4001. what is indicated?

- A. The activities are independent, with Activity 4001 starting 15 days earlier than the start of Activity 5001
- B. These activities are sequential, with Activity 4001 starting 15 days earlier than the start of Activity 3001.
- C. These activities are partially concurrent, with Activity 4001 starting 15 days after the start of Activity 3001

Answer: C

Explanation:

* Relationship Analysis:

Activity 4001 starts 15 days after Activity 3001 begins, based on their logical dependency (SS +15).

This indicates partial concurrency, as both activities overlap in execution.

* Evaluation of Other Options:

A: Incorrect, as the statement refers to Activity 5001, not 3001.

C: Incorrect, as Activity 4001 does not start before Activity 3001.

* Verification with PSP Guidelines:

PSP guidelines stress precise interpretation of activity relationships (Ref: PSP Study Guide, Chapter 2A: Logical Relationships and Lags).

NEW QUESTION # 191

Why does activity 1001 have two successor activities?

ID	Activity	Logic			Normal Schedule		Crashed Schedule	
		Succ.	Rel.	Lag	Days	Direct Costs	Days	Direct Costs
1000	General Conditions	11001	FF		1072	\$3,080,000	910	\$2,902,900
1001	Preliminary Civil Work	1000 2001 7001	SS FS FS		85	\$563,000	67	\$728,000
2001	River Diversion Stage 1	2002	FS		92	\$150,000	75	\$190,000
2002	River Diversion Stage 2	2003	FS		38	\$25,000	28	35,000
2003	River Diversion Dam	2004 3001	FS FS		15	\$18,000	11	\$20,000
2004	River Diversion to Pipeline	3001 7001	FS FS		38	\$96,000	38	\$96,000
3001	Excavation, Dam Site	4001 4001 5001 5001 7001	SS FF SS FF FS	15 15 65 65	30	\$482,000	100	\$515,000
4001	Excavation, Spillway	5001 5001 9001	SS FF FS	45 45	152	\$608,000	118	\$652,000
5001	Drill and Grout Dam Site	6001	FS		102	\$637,000	92	\$650,000
6001	Rock Fill: to elevation 25	6002	FS		140	\$1,352,000	105	\$1,470,000
6002	Rock Fill: to elevation 38	6003	FS		115	\$969,000	95	\$1,125,000
6003	Rock Fill: to elevation 50	8001 9002 9002 9003	FS SS FF FS	65 65	152	\$1,360,000	113	\$1,540,000
7001	Permanent Roads	11001 9004	FS FS		48	\$180,000	38	\$205,000
8001	Valve House Embankment	9004	FS		28	\$28,000	22	\$36,000
9001	Spillway – Concrete	11001 9002 9003	FS FS FS		175	\$1,120,000	155	\$1,305,000
9002	Dam Concrete Facing – Concrete	1001 9005	FS FS		180	\$1,260,000	160	\$1,485,000
9003	Inlet Tower – Concrete 1 of 2	9005	FS	7	70	\$275,000	65	\$295,000
9004	Valve House – Concrete	10002	FS	7	72	\$245,000	66	\$265,000
9005	Inlet Tower – Concrete 2 of 2	10001	FS	7	35	\$28,000	35	\$28,000
10001	Inlet Tower – Complete	11001	FS		25	\$147,000	25	\$147,000

- A. Because the problem could not effectively work with only one successor
- B. Because the duration of activities 2001, 2002 and 200.f require two successors
- C. Because there are two defined logic paths for the work
- D. Because the late finish of 1001 and the late start of 7001 require two successors

Answer: C

NEW QUESTION # 192

.....

Test AACE-PSP Collection Pdf: <https://www.actualvce.com/AACE-International/AACE-PSP-valid-vce-dumps.html>

- New AACE-PSP Test Answers □ New AACE-PSP Dumps Sheet □ Valid Test AACE-PSP Braindumps □ Search for 「 AACE-PSP 」 and download it for free immediately on □ www.testsimulate.com □ Valid AACE-PSP Exam Fee
- Three Easy-to-Use and Compatible Formats of AACE International AACE-PSP Practice Test □ Simply search for □ AACE-PSP □ for free download on □ www.pdfvce.com □ □AACE-PSP Simulated Test
- Three Easy-to-Use and Compatible Formats of AACE International AACE-PSP Practice Test □ Search for ➡ AACE-PSP □ and obtain a free download on （ www.examsreviews.com ） □New AACE-PSP Test Answers
- Quiz 2025 AACE International AACE-PSP: Planning & Scheduling Professional (PSP) Exam – High Pass-Rate Test Engine □ Easily obtain □ AACE-PSP □ for free download through ⇒ www.pdfvce.com ⇐ 📄AACE-PSP Vce Format
- Free Download Test AACE-PSP Engine - Updated Test AACE-PSP Collection Pdf: Planning & Scheduling Professional (PSP) Exam □ Search for □ AACE-PSP □ on ⇒ www.examdiscuss.com ⇐ immediately to obtain a free download □ □Latest AACE-PSP Exam Test
- AACE-PSP - Reliable Test Planning & Scheduling Professional (PSP) Exam Engine □ Copy URL 「 www.pdfvce.com 」 open and search for “ AACE-PSP ” to download for free □Vce AACE-PSP Exam
- Simplified AACE-PSP Guide Dump is an Easy to Be Mastered Training Materials □ Simply search for ☀ AACE-PSP □☀□ for free download on ➡ www.free4dump.com □ □AACE-PSP PDF Questions
- Free Download Test AACE-PSP Engine - Updated Test AACE-PSP Collection Pdf: Planning & Scheduling Professional (PSP) Exam □ Enter □ www.pdfvce.com □ and search for { AACE-PSP } to download for free □AACE-PSP Printable PDF
- Pass-Sure Test AACE-PSP Engine - Pass AACE-PSP Exam □ Open website ➡ www.free4dump.com □ and search for ▷ AACE-PSP ◁ for free download □AACE-PSP Vce Format
- New AACE-PSP Dumps Sheet □ Latest AACE-PSP Braindumps □ AACE-PSP Vce Format □ Copy URL ► www.pdfvce.com ◀ open and search for 《 AACE-PSP 》 to download for free □Valid AACE-PSP Exam Fee
- Efficient Test AACE-PSP Engine by www.real4dumps.com □ Search for □ AACE-PSP □ and download it for free immediately on▷ www.real4dumps.com◁ □AACE-PSP Valid Exam Registration
- infofitsoftware.com, pct.edu.pk, www.stes.tyc.edu.tw, gedsimekong.org, huohuohtd.com, myportal.utt.edu.tt, myportal.utt.edu.tt, myportal.utt.edu.tt, myportal.utt.edu.tt, myportal.utt.edu.tt, myportal.utt.edu.tt, myportal.utt.edu.tt, myportal.utt.edu.tt, myportal.utt.edu.tt, myportal.utt.edu.tt, myportal.utt.edu.tt, myportal.utt.edu.tt, myportal.utt.edu.tt, myportal.utt.edu.tt, myportal.utt.edu.tt, myportal.utt.edu.tt, myportal.utt.edu.tt, iachm.com, akibaniya829.blogspot.com, Disposable vapes

DOWNLOAD the newest ActualVCE AACE-PSP PDF dumps from Cloud Storage for free: https://drive.google.com/open?id=1VK1gWUEYeS9svRa7Q5x_fhHEBo1wn-6r
