

# Quiz AACE International - AACE-PSP - Planning & Scheduling Professional (PSP) Exam–Professional Valid Braindumps Questions



P.S. Free & New AACE-PSP dumps are available on Google Drive shared by Actual4Cert: <https://drive.google.com/open?id=1OgnC-33n0N4Vzu4wlmzJUCXO199BEhzX>

Do you want to pass your exam by using the latest time? If you do, you can choose the AACE-PSP study guide of us. We can help you pass the exam just one time. With experienced experts to compile and verify the AACE-PSP exam dumps, the quality and accuracy can be guaranteed. Therefore, you just need to spend 48 to 72 hours on training, you can pass the exam. In addition, we offer you free demo to have a try before buying AACE-PSP Study Guide, so that you can know what the complete version is like. Our online and offline chat service staff will give you reply of all your confusions about the AACE-PSP exam dumps.

The social environment is constantly changing, and our AACE-PSP guide quiz is also advancing with the times. We have all kinds of experiences on the AACE-PSP study braindumps for many years, so we know that the content of the exam is related to real-time information. The content of AACE-PSP Exam Materials is constantly updated. Our professional experts have been specializing in this career for over ten years. And we can always provide with you the most accurate and valid AACE-PSP learning guide.

>> Valid Braindumps AACE-PSP Questions <<

## How to Crack AACE International AACE-PSP Certification Exam Easily?

We have the free demo for the AACE-PSP study guide, it will help you to have a better understanding of the exam dumps, if you decide to buy and pay for it, we will send the downloading link and password to you within 10 minutes, and if you don't receive it, please contact to our service staff, we will deal with the problem for you immediately. What's more, free update for the AACE-PSP Study Guide for 365 days, and the update version will send to you by email automatically, therefore you can have the latest information for the Planning & Scheduling Professional (PSP) Exam.

The AACE-PSP Certification Exam is designed to test the skills and knowledge required to be a successful project planning and scheduling professional. By earning the certification, professionals demonstrate their commitment to their career and their ability to apply the best practices and techniques in their work. Planning & Scheduling Professional (PSP) Exam certification provides professionals with a competitive edge in the job market and opens up new career opportunities. Additionally, the certification helps organizations identify professionals who are capable of delivering successful projects on time and within budget.


## AACE International Planning & Scheduling Professional (PSP) Exam Sample Questions (Q105-Q110):

### NEW QUESTION # 105

Identify the late finish to develop plans and specs.

Refer to the following table and diagram to answer the following questions. Consider this to be the entire network. The diagram is incomplete. This table represents activities, predecessors and durations for a hazardous waste incineration facility.

Activity	Description	Predecessors	Duration (months)
A	Develop information for public hearings	-	3
B	Hold public hearings	A	3
C	Develop draft plans and specifications	A	5
D	Contact stakeholders and others	A	7
E	Obtain permits	B, C	3
F	Order equipment for facility	B	4
G	Procure and prepare land.	B	6
H	Construct facility	D, E, F & G	8
I	Approval of operating procedures	D	6
J	Install equipment, staff, faculty	F	9

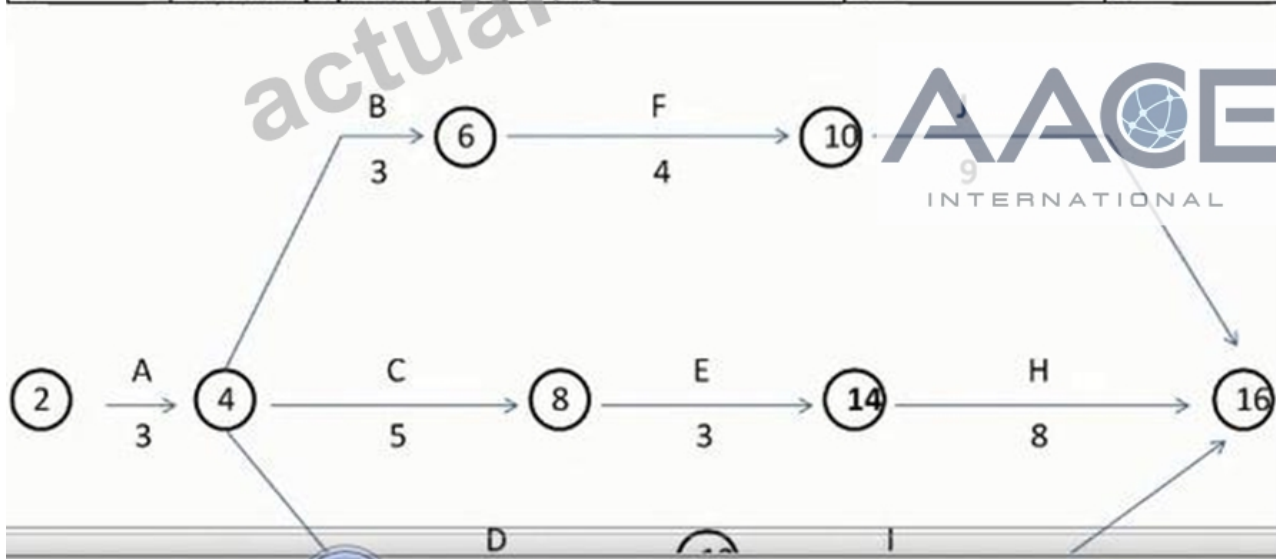

- A. 7 months.
- B. 10 months.
- C. 8 months.
- D. 9 months.


Answer: D

**NEW QUESTION # 106**

What is the free float for Activity F?

Refer to the following table and diagram to answer the following questions. Consider this to be the entire network. The diagram is incomplete. This table represents activities, predecessors and durations for a hazardous waste incineration facility.

Activity	Description	Predecessors	Duration (months)
A	Develop information for public hearings	-	3
B	Hold public hearings	A	3
C	Develop draft plans and specifications	A	5
D	Contact stakeholders and others	A	7
E	Obtain permits	B, C	3
F	Order equipment for facility	B	4
G	Procure and prepare land.	B	6
H	Construct facility	D, E, F & G	8
I	Approval of operating procedures	D	6
J	Install equipment, staff, faculty	F	9

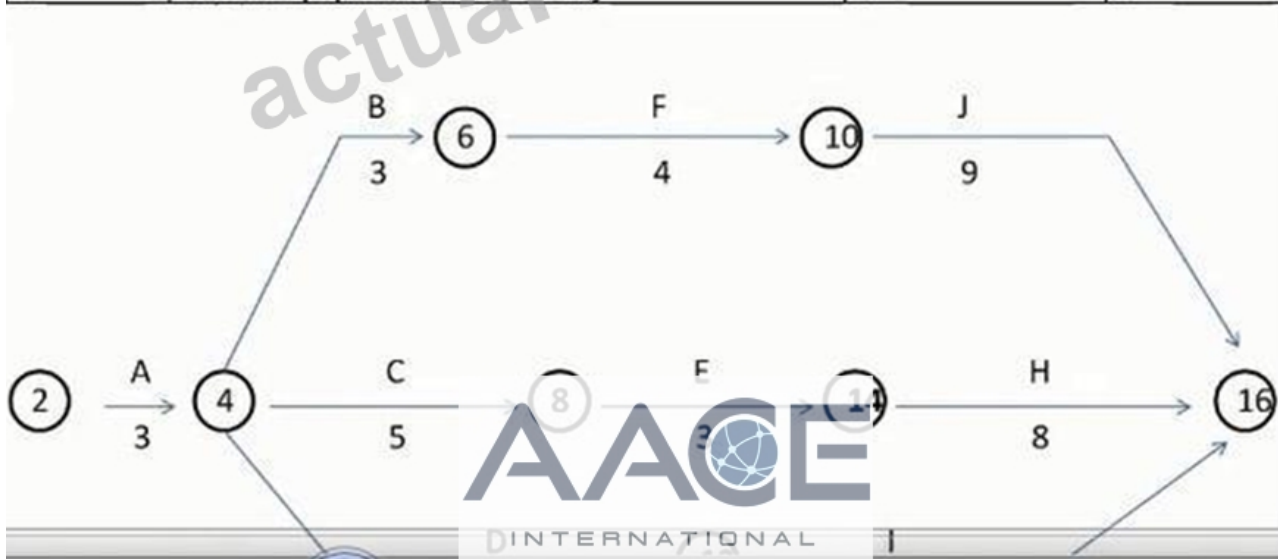

- A. 1 months.
- B. 3 months.
- C. 2 month.
- D. 0 months.

Answer: D

#### NEW QUESTION # 107

If after calculating a schedule an activity exhibits negative total float, which of the following is certain? The activity

- A. Is a milestone.
- B. Was completed in the past.
- C. Has yet to be completed.
- D. It is on the critical path.

Answer: C

#### NEW QUESTION # 108

What owner action could have mitigated the late completion of the project?

- A. Hire a more senior project manager.
- B. Prepare better structural steel drawings.
- C. Use a procurement agent to monitor and expedite equipment deliveries.
- D. Self-perform more of the work.

**Answer: C**

Explanation:

\* Mitigating Late Completion:

A procurement agent could monitor and expedite long-lead equipment, reducing delivery delays that often affect project timelines.

\* Evaluation of Other Options:

A: Hiring a senior project manager may not address the specific issue.

B: Self-performing may not resolve procurement delays.

D: Better structural steel drawings relate to design, not equipment delays.

\* Verification with PSP Guidelines:

PSP emphasizes early identification and mitigation of procurement risks (Ref: PSP Study Guide, Chapter 2B: Procurement and Supply Chain Management).

### NEW QUESTION # 109

Using the normal schedule, what is the early finish date and total float of Activity 10002?

- A. 21 Dec 2023. and 4 days of total float
- B. 17 Dec 2023. and 4 days of total float
- C. 24 Dec 2023. and 24 days of tree float
- D. 24 Nov 2023. and 24 days of tree float

**Answer: A**

Explanation:

The early finish date and total float are determined using CPM calculations. The PSP Study Guide outlines that early finish is calculated as the early start date plus activity duration, adjusted for calendar constraints (PSP Study Guide, Subchapter 2.2.5, "Constraints and Calendars").

Steps:

Determine early start using forward pass calculations.

Add the activity duration.

Consider non-working days or holidays as per the project calendar.

Calculate float as the difference between late start and early start or late finish and early finish.

### NEW QUESTION # 110

.....

When you are struggling with those troublesome reference books; when you feel helpless to be productive during the process of preparing AACE-PSP exams; when you have difficulty in making full use of your sporadic time and avoiding procrastination. It is time for you to realize the importance of our AACE-PSP Test Prep, which can help you solve these annoyance and obtain a AACE-PSP certificate in a more efficient and productive way. Not only will you be able to pass any AACE-PSP test, but will gets higher score, if you choose our AACE-PSP study materials.

**AACE-PSP Valid Test Dumps:** <https://www.actual4cert.com/AACE-PSP-real-questions.html>

- New Released AACE International AACE-PSP Questions Verified by Experts [2026]  Search for  AACE-PSP  and download it for free on [www.validtorrent.com](http://www.validtorrent.com)  website  Valid Braindumps AACE-PSP Free
- Latest Released AACE International Valid Braindumps AACE-PSP Questions - AACE-PSP Planning & Scheduling Professional (PSP) Exam  The page for free download of  AACE-PSP  on [www.pdfvce.com](http://www.pdfvce.com)  will open immediately  Study AACE-PSP Dumps
- Formal AACE-PSP Test  AACE-PSP New Dumps Questions  100% AACE-PSP Correct Answers  Open [www.practicevce.com](http://www.practicevce.com)  enter 「 AACE-PSP 」 and obtain a free download  Exams AACE-PSP Torrent
- My Review On AACE International AACE-PSP Exam Questions  Search for 「 AACE-PSP 」 and easily obtain a free download on  [www.pdfvce.com](http://www.pdfvce.com)   AACE-PSP Valid Exam Syllabus
- Hot Valid Braindumps AACE-PSP Questions 100% Pass | High-quality AACE-PSP Valid Test Dumps: Planning &

