

# Quiz The Best AACE International - Latest Test AACE-PSP Simulations



BONUS!!! Download part of RealExamFree AACE-PSP dumps for free: [https://drive.google.com/open?id=1Ry0kyilpzNvHrVbw00KKrk1Hr6tmZx\\_](https://drive.google.com/open?id=1Ry0kyilpzNvHrVbw00KKrk1Hr6tmZx_)

The RealExamFree is one of the leading AACE International AACE-PSP exam preparation study material providers in the market. The RealExamFree offers valid, updated, and real Planning & Scheduling Professional (PSP) Exam AACE-PSP exam practice test questions that assist you in your AACE-PSP Exam Preparation. The AACE International AACE-PSP exam questions are designed and verified by experienced and qualified AACE International exam trainers.

There is no need to worry about virus on buying electronic products. For RealExamFree have created an absolutely safe environment and our exam question are free of virus attack. We make endless efforts to assess and evaluate our AACE-PSP exam question' reliability for a long time and put forward a guaranteed purchasing scheme. If there is any doubt about it, professional personnel will handle this at first time, and you can also have their remotely online guidance to install and use our AACE-PSP Test Torrent.

**>> Latest Test AACE-PSP Simulations <<**

## Latest AACE-PSP Test Simulator - Dumps AACE-PSP Free Download

Do you want to pass AACE-PSP exam and get the related certification within the minimum time and effort? If you would like to give me a positive answer, you really should keep a close eye on our website since you can find the best study material in here--our AACE-PSP training materials. We have helped millions of thousands of candidates to prepare for the AACE-PSP Exam and all of them have got a fruitful outcome, I wish you could be one of the beneficiaries of our training materials in the near future. The advantages of our AACE-PSP test prep are more than you can imagine.

AACE International AACE-PSP (Planning & Scheduling Professional) Exam is a certification program that is designed to validate the skills and knowledge of individuals working in the planning and scheduling field. Planning & Scheduling Professional (PSP) Exam certification is recognized globally and is highly valued by employers in the industry. The AACE-PSP Exam covers a wide range of topics, including project planning and control, scheduling, cost management, risk management, and project communication.

## How to study the Planning & Scheduling Professional (PSP) Exam

In general, the education and professional experience of an applicant are the primary sources that prepare the person for the test. As mentioned in the eligibility criteria for the exam, the applicant must have at least 4 to 8 years of industry experience in the field which itself is preparatory material. There are, however, other ways to prepare for the test. AACE itself provides a distant learning opportunity through its website for which applicants can sign up. AACE conducts review sessions and annual meetings in which the participation of an applicant can prove to be very helpful as they will be able to participate and listen to discussions on the topics of planning and scheduling.

Participants must search for the answers to the following questions if they wish to prepare the best for the exam:

- Why is planning important?
- Why is scheduling important?
- What is a CPM schedule?
- What is planning?

Furthermore, **PSP exam dumps pdf** and **PSP practice exams** are available online, and students are highly encouraged to study those exam dumps as they are the best study materials. As always, We recommend a combination of hands-on experience, completion of the training course, and self-study in the areas described in the Exam Outline section of this exam guide as preparation for this exam. After all sorts of study, test your understanding by taking the **PSP practice exams**. Hover on to AACE's Website and take a look at study materials provided for the exam. Check for the topics mentioned in the Exam Outline section of this guide to review the online documentation, tip sheets, and user guides and study the details relevant to those topics. Refer to the links at the end of this document for more study material. For further exam self-study materials, refer to the links down below.

## **AACE International Planning & Scheduling Professional (PSP) Exam Sample Questions (Q188-Q193):**

### **NEW QUESTION # 188**

Scenario: You are providing construction management services for a small office building project. Your duties include reviewing and approving the contractor's baseline schedule. The contractor has submitted the first baseline schedule for the project.

The contractor subsequently submits a CPM schedule for its baseline schedule submittal. As part of your review, you look at the durations for each activity in the schedule. How do you determine if a duration of 10 work days for drywall installation is accurate?

- A. Review the location of drywall work in the contract drawings
- **B. Review the drywall quantity, methods and location with the project superintendent to determine a reasonable duration**
- C. Divide the quantity of drywall by the construction crew's dairy production rate for this work
- D. The duration for drywall installation should De proportional to how critical the activity is


**Answer: B**

### **NEW QUESTION # 189**

Identify the late finish to develop plans and specs.

Refer to the following table and diagram to answer the following questions. Consider this to be the entire network. The diagram is incomplete. This table represents activities, predecessors and durations for a hazardous waste incineration facility.

Activity	Description	Predecessors	Duration (months)
A	Develop information for public hearings	-	3
B	Hold public hearings	A	3
C	Develop draft plans and specifications	A	5
D	Contact stakeholders and others	A	7
E	Obtain permits	B, C	3
F	Order equipment for facility	B	4
G	Procure and prepare land	B	6
H	Construct facility	D, E, F & G	8
I	Develop operating procedures	D	6
J	Install equipment, staff, facility	F	9

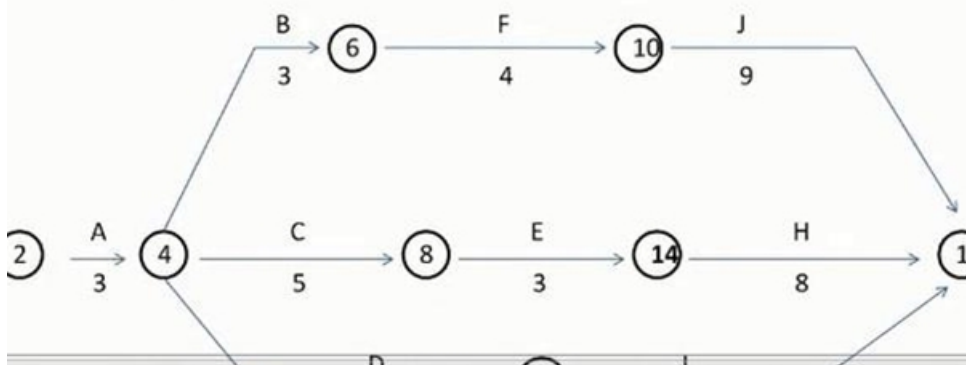

- A. 10 months.
- B. 8 months.
- C. 7 months.
- D. 9 months.

Answer: D

#### NEW QUESTION # 190

How many work days does it take to move the product from testing to sale?

<div style="display: flex; align-items: center;"> <div> <b>Product Scenario #4</b>            Product Development has established the following items with the duration required for each need to be accomplished in order for the release of a new product. Once Product Testing is complete, both Release for Manufacture and Drafting of a product manual can proceed. Proofing and correction of the manual is required prior to printing. Manufacturing and printing of the manual are required to package and make the product available.         </div> </div>			
ID	Activity Description	Duration	Predecessors
A	Complete Product Testing	30	-
B	Release for Manufacture	0	A
C	Draft Product Manual	20	A
D	Manufacture Product	60	B
E	Proof Product Manual	10	C
F	Print Project Manual	20	E
G	Package Product	10	D, F
H	Product Available Date	0	G

- A. 60.
- B. 100.
- C. 90.
- D. 70.

**Answer: B**

Explanation:

\* Understanding the Timeline:

The total time from testing (Activity A) to the release of the product (Activity H) involves sequential tasks.

Calculate the durations of the critical path:

Activity A: 30 days

Activity B: 0 days

Activity D: 60 days

Activity F: 20 days

Activity G: 10 days

\* Summing Durations:

Total duration =  $30 + 0 + 60 + 20 + 10 = 100$  days.

\* Verification with PSP Guidelines:

The PSP Study Guide emphasizes critical path analysis for determining the project timeline (Ref: PSP Study Guide, Chapter 2A: Critical Path Method).

### **NEW QUESTION # 191**

What activities are concurrent to Activity 2001 in the "normal" schedule?

ID	Activity	Logic			Normal Schedule		Crashed Schedule	
		Succ.	Rel.	Lag	Days	Direct Costs	Days	Direct Costs
1000	General Conditions	11001	FF		1072	\$3,080,000	910	\$2,902,900
1001	Preliminary Civil Work	1000 2001 7001	SS FS FS		85	\$563,000	67	\$728,000
2001	River Diversion Stage 1	2002	FS		92	\$150,000	75	\$190,000
2002	River Diversion Stage 2	2003	FS		38	\$25,000	28	35,000
2003	River Diversion Dam	2004 3001	FS FS		15	\$18,000	11	\$20,000
2004	River Diversion to Pipeline	3001 7001	FS FS		38	\$96,000	38	\$96,000
3001	Excavation, Dam Site	4001 4001 5001 5001 7001	SS FF SS FF FS	15 15 65 65	30	\$482,000	100	\$515,000
4001	Excavation, Spillway	5001 5001 9001	SS FF FS	45 45	152	\$608,000	118	\$692,000
5001	Drill and Grout Dam Site	6001	FS		102	\$637,000	92	\$650,000
6001	Rock Fill: to elevation 25	6002	FS		140	\$1,352,000	105	\$1,470,000
6002	Rock Fill: to elevation 38	6003	FS		115	\$969,000	95	\$1,125,000
6003	Rock Fill: to elevation 50	8001 9002 9002 9003	FS SS FF FS	65 65	152	\$1,360,000	113	\$1,540,000
7001	Permanent Roads	11001 9004	FS FS		48	\$180,000	38	\$205,000
8001	Valve House Embankment	9004	FS		28	\$28,000	22	\$36,000
9001	Spillway – Concrete	11001 9002 9003	FS FS FS		175	\$1,120,000	155	\$1,305,000
9002	Dam Concrete Facing – Concrete	1001 9005	FS FS		180	\$1,260,000	160	\$1,485,000
9003	Inlet Tower – Concrete 1 of 2	9005	FS	7	70	\$275,000	65	\$295,000
9004	Valve House – Concrete	10002	FS	7	72	\$245,000	66	\$265,000
9005	Inlet Tower – Concrete 2 of 2	10001	FS	7	35	\$28,000	35	\$28,000
10001	Inlet Tower – Complete	11001	FS		25	\$147,000	25	\$147,000
	Valve House –	10001	FS		24	\$132,000	24	\$132,000

- A. 1000.



- B. 1001.
- C. 2003.
- **D. 7001.**

**Answer: D**

#### NEW QUESTION # 192

Using the "normal" schedule, and assuming you are billing on the last day of the month for previous month and for appropriate partial months, how many invoices will you have for this project?

- A. 37.
- **B. 42.**
- C. 40.
- D. 36.

**Answer: B**

Explanation:

\* Understanding the Requirement:

The "normal" schedule duration is 1072 days for Activity 1000 (General Conditions).

Billing occurs at the end of each month for the previous month.

Partial months are included in billing cycles.

\* Total Project Duration in Months:

Total days: 1072.

Convert to months:  $1072 \div 26 \approx 41.23$  months.

Include partial months, which adds 1 additional invoice.

\* Total Invoices:

Full months: 35.

Partial months: 7 (assuming each partial month is rounded up to include invoicing).

Total invoices = 35 + 7 = 42.

\* PSP Principles Cross-Verification:

PSP guidelines emphasize accurate conversion of schedule durations into calendar billing periods for effective cash flow management (Ref: PSP Study Guide, Chapter 2B: Schedule Output and Deliverables).

#### NEW QUESTION # 193

.....

RealExamFree AACE International AACE-PSP practice exam support team cooperates with users to tie up any issues with the correct equipment. If Planning & Scheduling Professional (PSP) Exam (AACE-PSP) certification exam material changes, RealExamFree also issues updates free of charge for three months following the purchase of our Planning & Scheduling Professional (PSP) Exam (AACE-PSP) exam questions.

**Latest AACE-PSP Test Simulator:** <https://www.realexamfree.com/AACE-PSP-real-exam-dumps.html>

- The Best AACE International - Latest Test AACE-PSP Simulations ☐ The page for free download of { AACE-PSP } on ☒ [www.free4dump.com](http://www.free4dump.com) ☐ ☒ will open immediately ☐ Valid AACE-PSP Exam Duration
- AACE-PSP Exam Torrent - AACE-PSP Practice Test - AACE-PSP Quiz Torrent ☐ Easily obtain ☐ AACE-PSP ☐ for free download through ☐ [www.pdfvce.com](http://www.pdfvce.com) ☐ 100% AACE-PSP Accuracy
- AACE-PSP Reliable Exam Materials ☐ AACE-PSP Study Material ☐ AACE-PSP Trustworthy Exam Content ☐ Enter ☐ [www.getvalidtest.com](http://www.getvalidtest.com) ☐ and search for ☒ AACE-PSP ☐ to download for free ☐ AACE-PSP Valid Test Papers
- AACE-PSP Reliable Exam Materials ☐ AACE-PSP Valid Test Papers ☐ Exam AACE-PSP Cram ☐ Search for ☐ [www.pdfvce.com](http://www.pdfvce.com) ☐ Upgrade AACE-PSP Dumps
- AACE-PSP Latest Exam Guide ☐ AACE-PSP Labs ☐ AACE-PSP Study Material ☐ Open website ☒ [www.testsdumps.com](http://www.testsdumps.com) ☐ and search for "AACE-PSP" for free download ☐ AACE-PSP Latest Test Guide
- The Best AACE International - Latest Test AACE-PSP Simulations ☐ Enter { [www.pdfvce.com](http://www.pdfvce.com) } and search for ☒ AACE-PSP ☐ to download for free ☐ 100% AACE-PSP Accuracy
- AACE-PSP Trustworthy Exam Content ☒ 100% AACE-PSP Accuracy ☐ AACE-PSP Latest Exam Answers ☒ Search for "AACE-PSP" on ☒ [www.actual4labs.com](http://www.actual4labs.com) ☐ ☒ immediately to obtain a free download ☐ AACE-PSP Labs

- Exam Dumps AACE-PSP Free ⇔ AACE-PSP Latest Exam Answers □ 100% AACE-PSP Accuracy □ Download ✓ AACE-PSP □ ✓ □ for free by simply entering ➡ [www.pdfvce.com](http://www.pdfvce.com) □ website □ AACE-PSP Labs
- AACE-PSP Exam Torrent - AACE-PSP Practice Test - AACE-PSP Quiz Torrent □ Open { [www.vceengine.com](http://www.vceengine.com) } and search for ( AACE-PSP ) to download exam materials for free □ Upgrade AACE-PSP Dumps
- 100% AACE-PSP Accuracy □ 100% AACE-PSP Accuracy □ AACE-PSP Latest Exam Answers □ Simply search for ▷ AACE-PSP ◁ for free download on ( [www.pdfvce.com](http://www.pdfvce.com) ) □ AACE-PSP Reliable Exam Materials
- New AACE-PSP Test Pattern □ 100% AACE-PSP Accuracy □ Exam Dumps AACE-PSP Free □ Enter □ [www.examsreviews.com](http://www.examsreviews.com) □ and search for 【 AACE-PSP 】 to download for free □ AACE-PSP Reliable Real Test
- [www.stes.tyc.edu.tw](http://www.stes.tyc.edu.tw), [www.stes.tyc.edu.tw](http://www.stes.tyc.edu.tw), [www.stes.tyc.edu.tw](http://www.stes.tyc.edu.tw), [myportal.utt.edu.tt](http://myportal.utt.edu.tt), [myportal.utt.edu.tt](http://myportal.utt.edu.tt), [myportal.utt.edu.tt](http://myportal.utt.edu.tt), [myportal.utt.edu.tt](http://myportal.utt.edu.tt), [myportal.utt.edu.tt](http://myportal.utt.edu.tt), [myportal.utt.edu.tt](http://myportal.utt.edu.tt), [myportal.utt.edu.tt](http://myportal.utt.edu.tt), [myportal.utt.edu.tt](http://myportal.utt.edu.tt), [myportal.utt.edu.tt](http://myportal.utt.edu.tt), [www.stes.tyc.edu.tw](http://www.stes.tyc.edu.tw), [www.stes.tyc.edu.tw](http://www.stes.tyc.edu.tw), [www.stes.tyc.edu.tw](http://www.stes.tyc.edu.tw), [www.stes.tyc.edu.tw](http://www.stes.tyc.edu.tw), [elearning.eauquardho.edu.so](http://elearning.eauquardho.edu.so), [ncon.edu.sa](http://ncon.edu.sa), [www.stes.tyc.edu.tw](http://www.stes.tyc.edu.tw), Disposable vapes

DOWNLOAD the newest RealExamFree AACE-PSP PDF dumps from Cloud Storage for free: [https://drive.google.com/open?id=1Ry0kyilpzNvHrVbw00KKrk1Hr6tmZx\\_](https://drive.google.com/open?id=1Ry0kyilpzNvHrVbw00KKrk1Hr6tmZx_)
